Project Performance Monitoring

Objective

- **Track project performance across:**
  - **Cost**
  - **Schedule**
  - **Scope**

Monitoring Approach

- Use of **Key Performance Indicators (KPIs)**
- Regular **status reviews and reporting**
- Comparison of **planned vs actual performance**

Control Mechanisms

- **Variance analysis**
- **Corrective action planning**
- **Continuous performance evaluation**

Management Insight

- Early identification of **delays and cost overruns**
- Enables **data-driven** decision making
- Ensures project remains aligned with **baseline plan**

Earned Value Analysis (EVA)

Purpose

- Evaluate project **performance** using **cost and schedule metrics**
- Compare **planned vs actual vs earned** progress

Key Metrics

- **Planned Value (PV):** Budgeted work
- **Earned Value (EV):** Work completed
- **Actual Cost (AC):** Cost incurred

Performance Indicators

- **CPI (Cost Performance Index)**
- **SPI (Schedule Performance Index)**

Management Insight

- **EV < PV → Schedule delay**
- **EV < AC → Cost overrun**
- Supports forecasting and corrective actions

Earned Value Analysis (EVA)

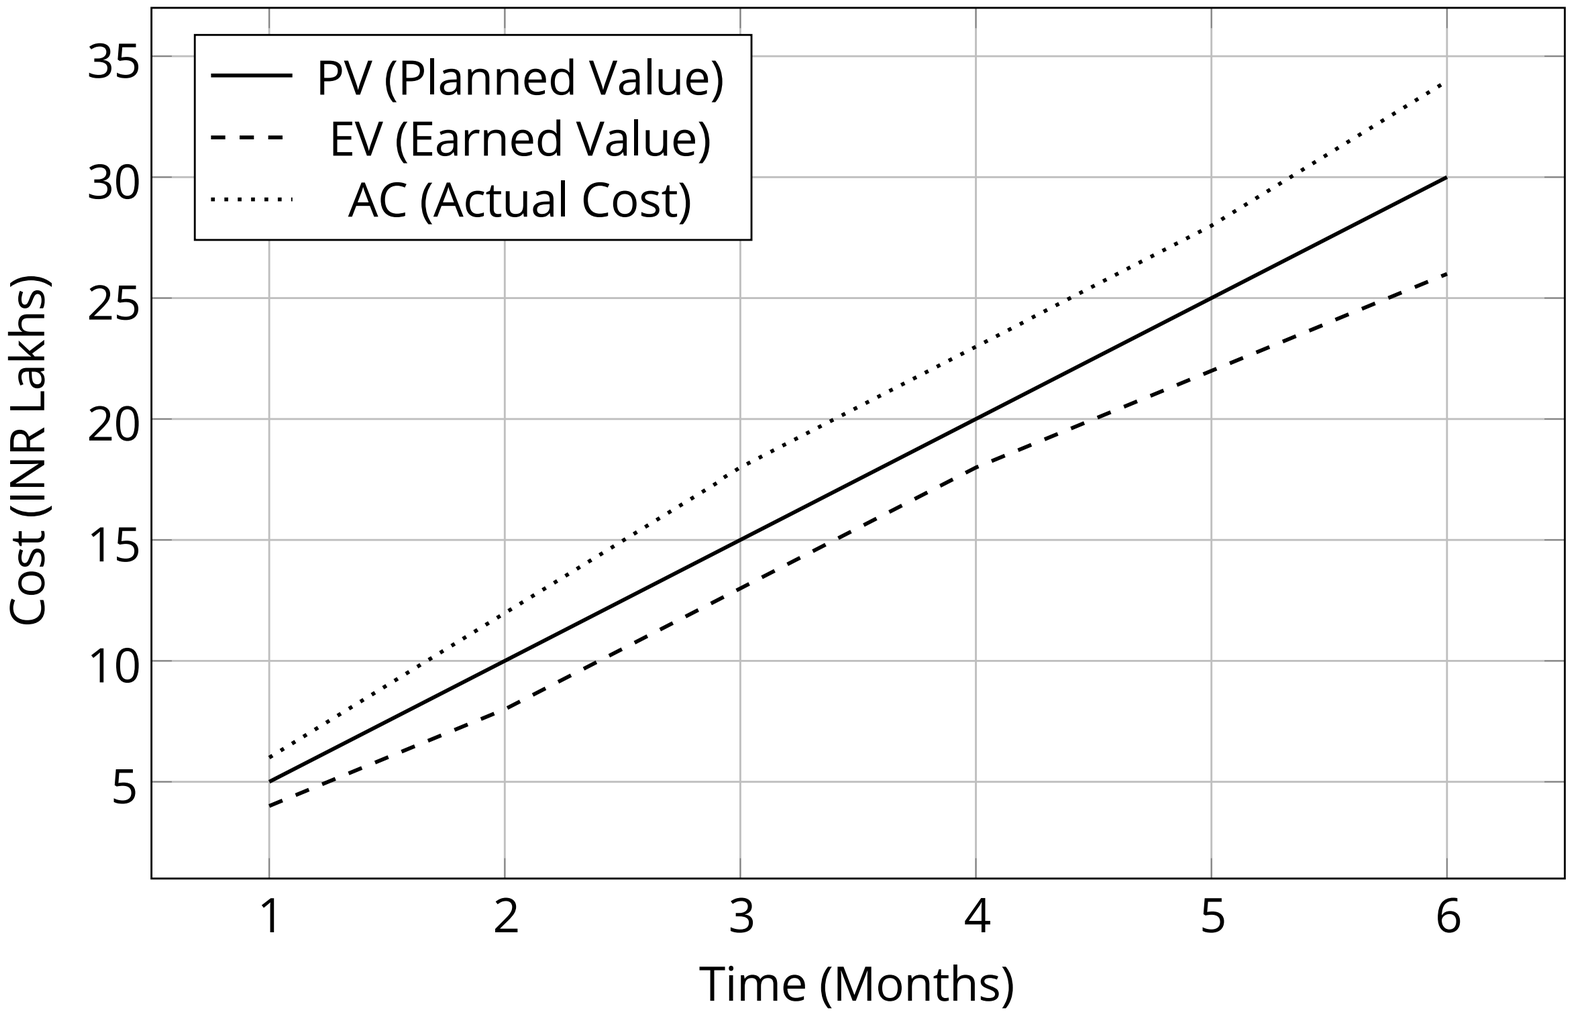

Project Risk Management

Objective

- **Identify, assess, and control** project risks proactively

Risk Management Process

- Risk Identification
- Risk Analysis (Probability & Impact)
- Risk Response Planning
- Risk Monitoring

Key Risks Identified

- Complexity of linguistic rules
- Resource constraints (expert availability)
- Data annotation delays

Management Strategies

- **Risk mitigation** and **contingency** planning
- Allocation of risk reserves
- Continuous monitoring through **RMMM plan**

Outcome

- Reduced uncertainty
- Improved project stability and predictability

Risk Assessment Matrix

Project Risks

- **R1:** Paninian grammar complexity
- **R2:** Limited expert availability
- **R3:** Data annotation delays
- **R4:** Minor operational inefficiencies

Risk Positioning

- **R1 → Critical Zone**
  - High probability + very high impact
- **R2 → High Risk Zone**
  - Moderate–high probability and impact
- **R3 → Medium Risk Zone**
  - Moderate impact, manageable
- **R4 → Low Risk Zone**
  - Low probability and impact

Management Insight
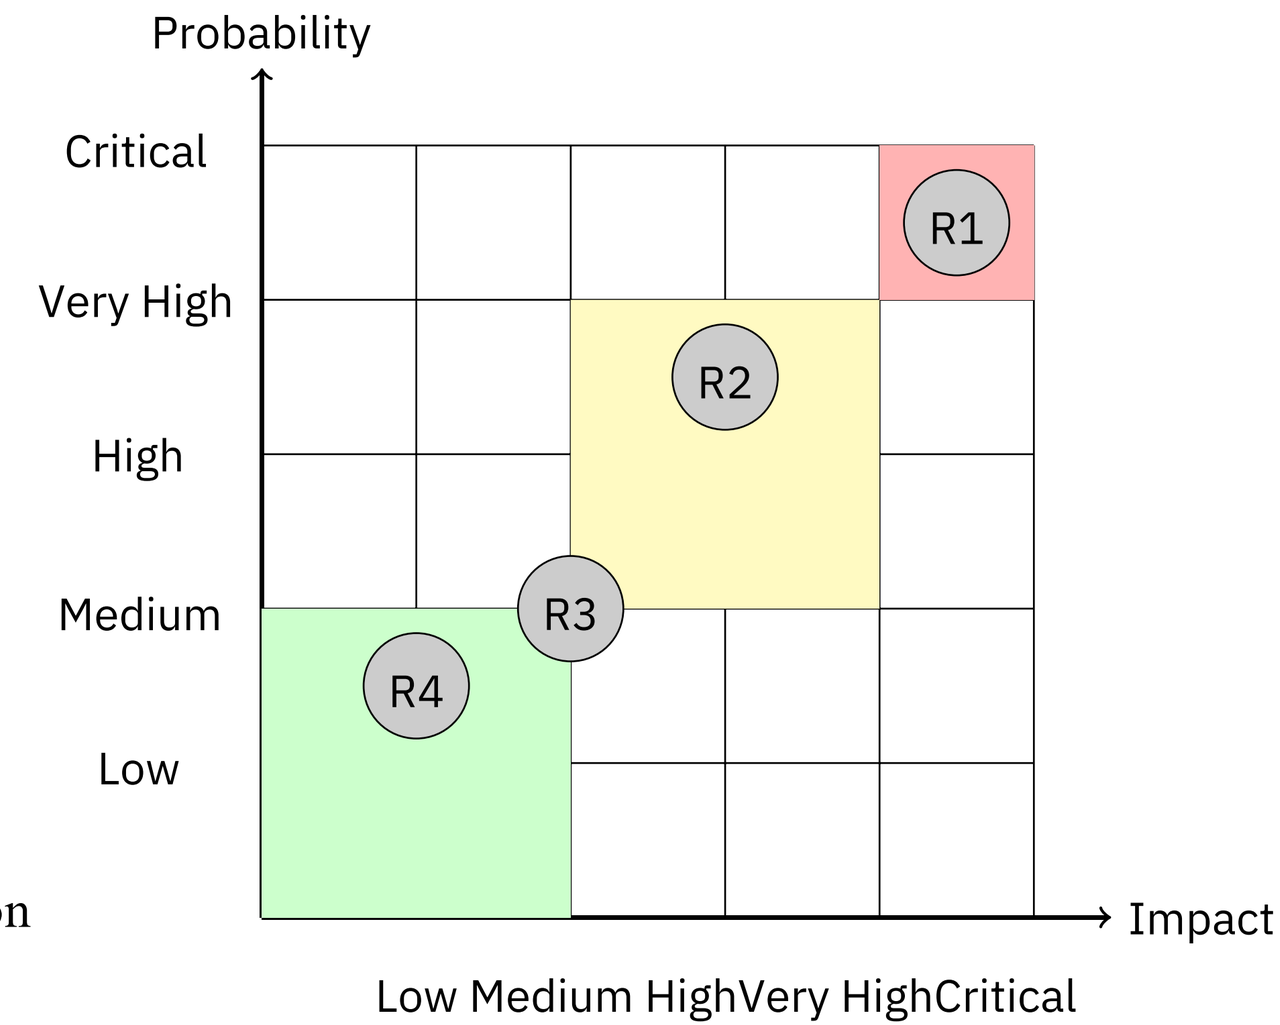
- Focus on **R1** and **R2** for immediate mitigation
- Monitor **R3**, accept/manage **R4**
